


SUMMARY

Details


to 1 November 2011

Start date	1 October 2008
Contractual end date	31 March 2013
Time left to expected completion date	31.48 %
Contract amount	GBP 25.5 million
Expenditure to date	GBP 17.64 million
Total employment days created	4.67 million
Payment on road construction wages	GBP 11.89 million

Livelihoods: Active RBGs: 392/750 RBG+SBG workers: 16,012 Est. final RBG wage: NRs 1,556M

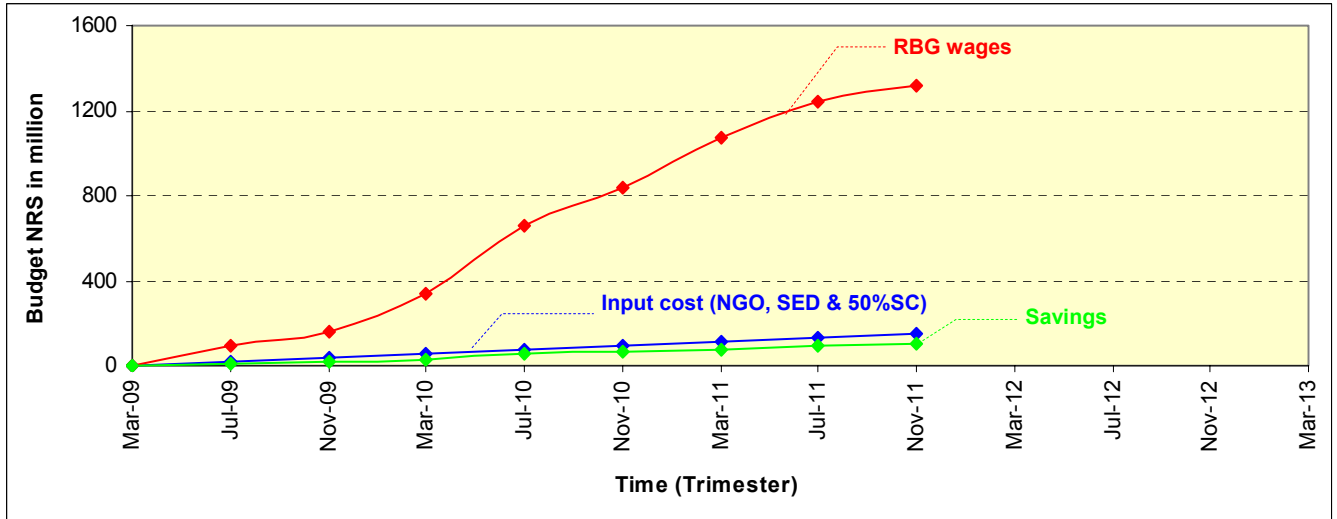

Road progress (Financial): Spent to date: NRs 1,675M Latest estimate: NRs 2,183M

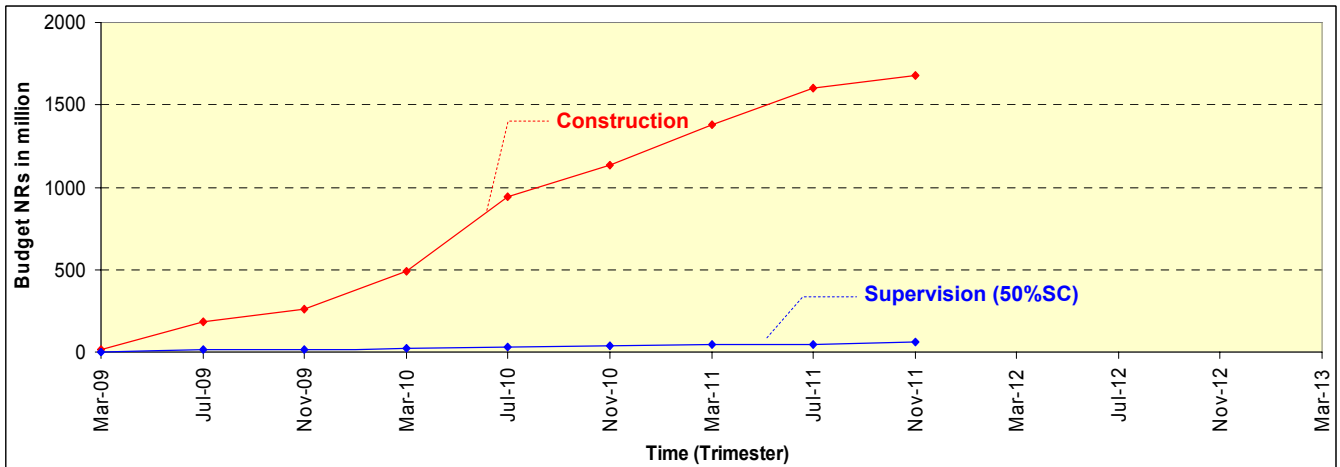

Road progress (Physical):

